


Legend

- CAM Beach - Phase 1 - 5 Non Rev Days 0 IN
- CAM Beach - Phase 2 - 5 Non Rev Days 0 IN
- CAM Beach - Phase 3 - 10 Rev Days 0 IN
- CAM Beach - Phase 4 - 7 Rev Days 0 IN
- CAM Beach - Phase 5 - 6 Rev Days 0 IN
- CAM Beach - Phase 6 - 7 Rev Days 0 IN

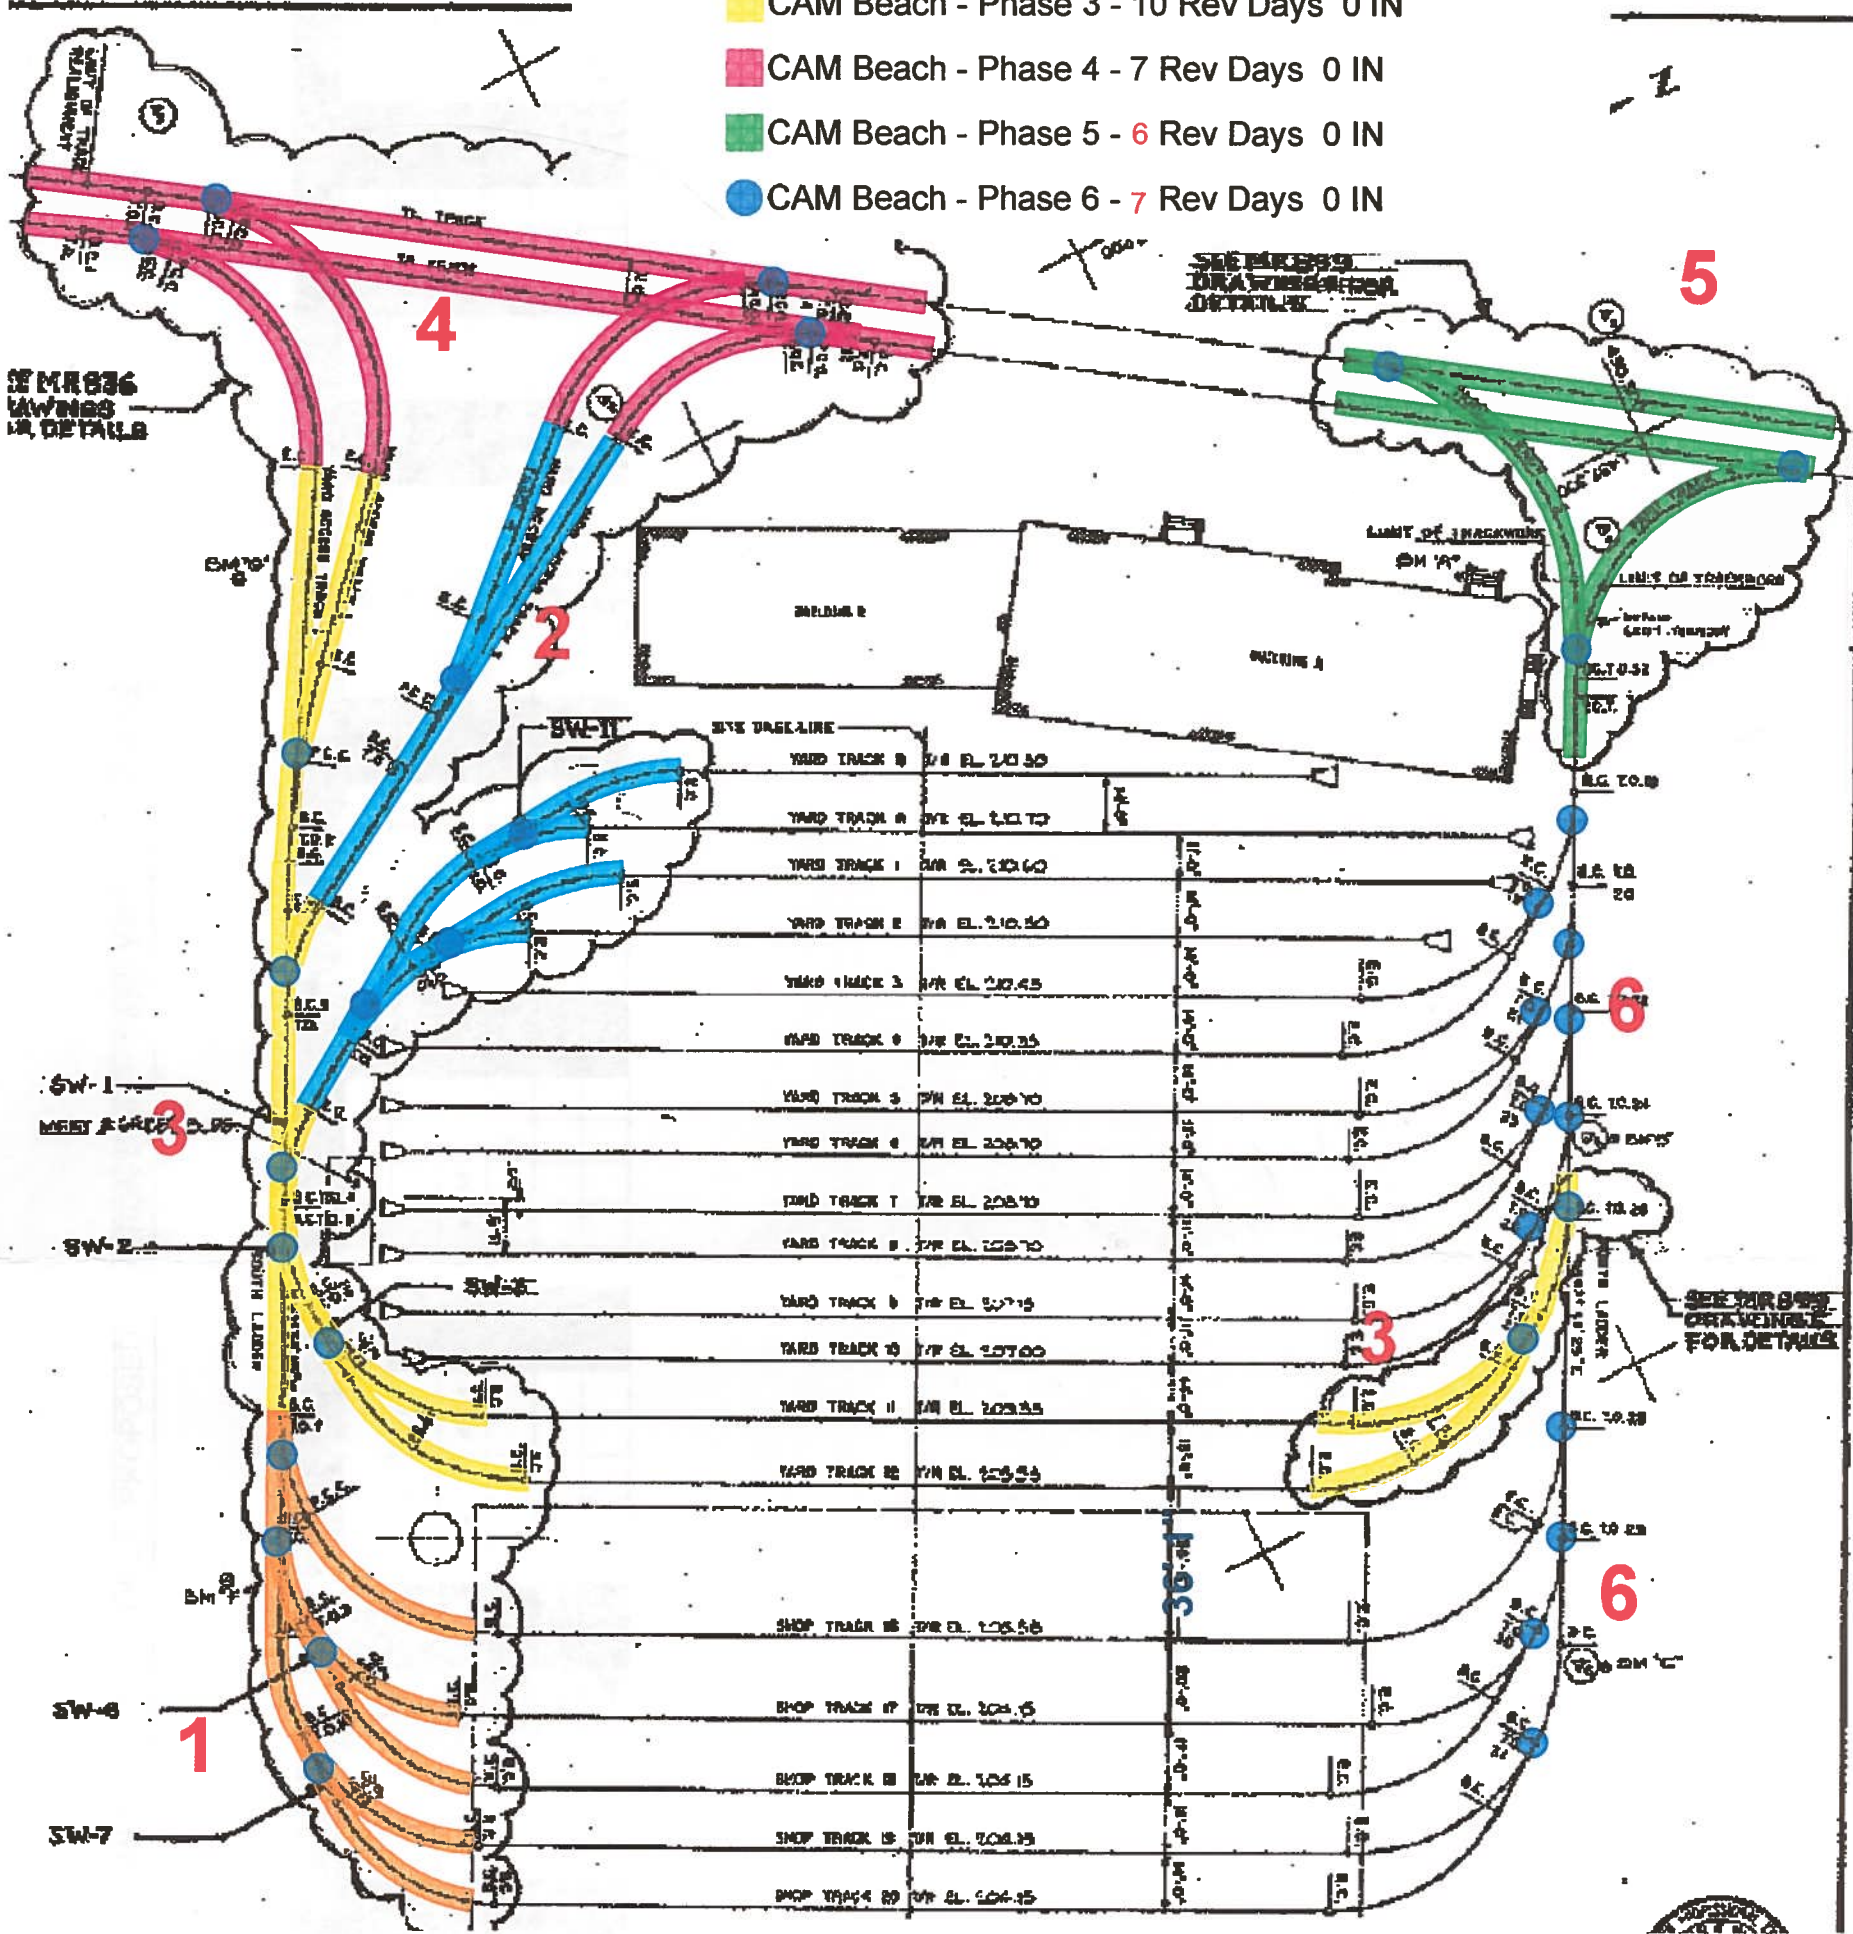

PHASE DESCRIPTIONS AND APPROXIMATE DURATIONS:

- Phase 1 - South East Ladder Track = 5 Non-Revenue Days
- Phase 2 - South Ladder Track (part A) = 5 Non-Revenue Days
- Phase 3 - South Ladder Track (part B) & North Ladder Track = 10 Revenue Days
- Phase 4 - South Ladder Entrance & M-Line = 7 Revenue Days
- Phase 5 - North Ladder Entrance and M-Line = 6 Revenue Days
- Phase 6 - North Ladder Track Switch Castings Refurbishment = 7 Revenue Days
